
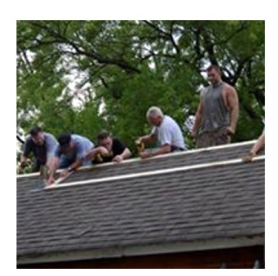


D
A
Y
O
N
E

The House of David Mission Project 2016

Removed old siding, started to frame in new room, began roof replacement, cut in kitchen window.



D
A
Y

SUNDAY
JULY 24

T
W
O





Finished framing, installed trusses, started sheeting, cut in windows & doorway in new addition, started house wrap, ran electric.

D
A
Y

MONDAY
JULY 25

T
H
R
E
E

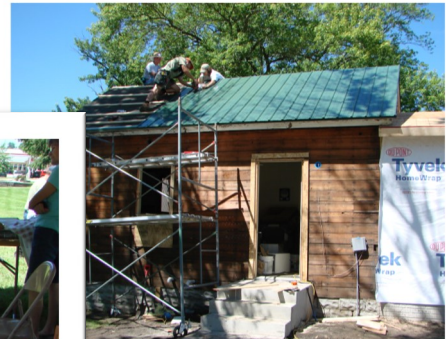

Continued roofing, started to hang drywall, added insulation on old house, finished house wrap, plumbing.





**TUESDAY
JULY 26**



Mudded & textured drywall , put in new kitchen & bath windows, continued with roof, & house cleaning, siding.

D

A

Y

WEDNESDAY

JULY 27





F

I



V

E

Painted new addition,
repaired walls, misc.
cleaning throughout the
house, siding & soffits.

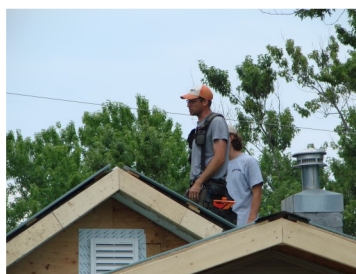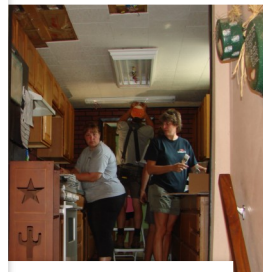

D

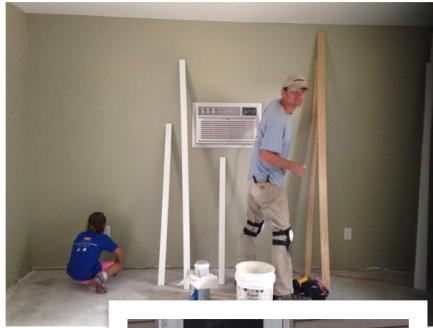

Put in doorbell,
smoke alarms,
finished lighting
& outlets, siding
& soffits.


A
Y

D



THURSDAY
JULY 28

Painting, hung
new curtains,
siding, roof trim.



SATURDAY
JULY 30



S

I

X



S

E

V

E

N



D
A
Y

SUNDAY
JULY 31

E
I
G
H
T



D
A
Y

MONDAY
AUGUST 1

N
I
N
E

Sprayed foam insulation
on foundation, installed
railings on fronts steps,
finished electrical.



Finished roofing and siding, house cleaning,
painted basement doors, painted back entry.

D

A

Y

TUESDAY
AUGUST 2

T

E

N

Painted living room,
dirt was brought in
for landscaping,



More to come...

The landscaping around David's house
will be done by some volunteers in the near
future....look for a final update next month.



D

A

Y

WEDNESDAY
AUGUST 3

E

L

E

L




E

V

E

N

Painted trim in living room,
installed flooring & woodwork in
new addition, put in dryer vent,
moved in appliances.

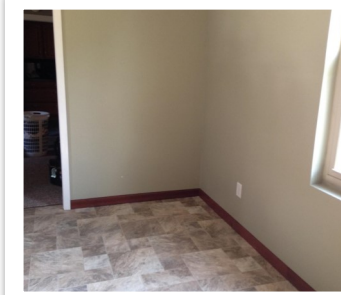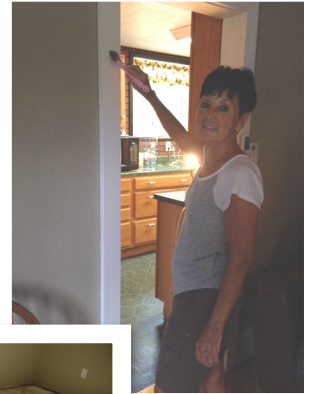

Thank you very much, love David
